




Department of Public Works  
Special Districts Division

# Snowdrop Road Project Status Update

April 4, 2022

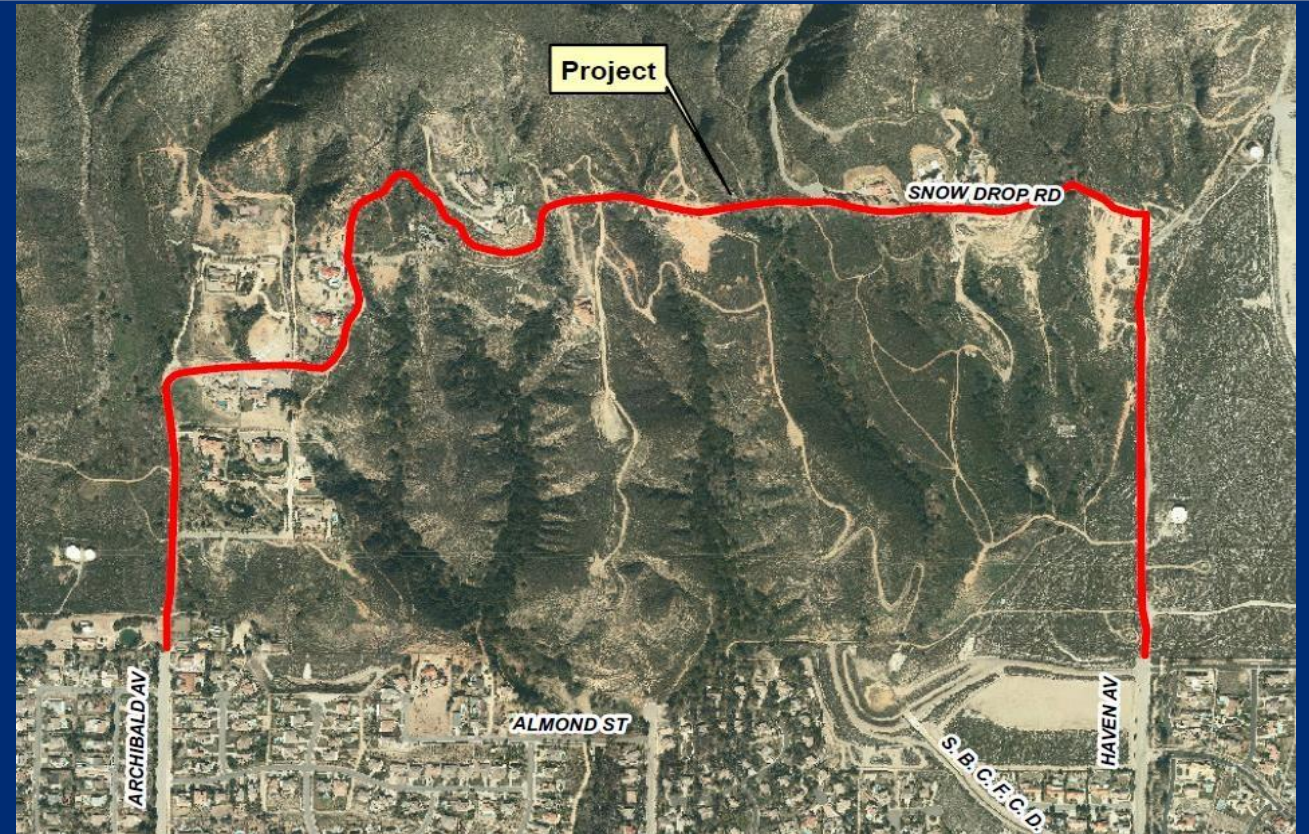



## Project Milestones

- April 6, 2021: Board of Supervisors approved the project bond
- April 15, 2021: Bond issued
- April 20, 2021: Board of Supervisors award of construction contract to Trinity Construction
- May 17, 2021: Groundbreaking Ceremony – Construction Started
- Summer 2022: Target completion date





## **CONSTRUCTION UPDATES**

- Storm drain structures are 90% completed
- Retaining walls are 80% completed
- Slopes earthwork is 75% completed
- Construction currently focusing on completing Christmas Canyon and retaining walls work
- Storm Water Management and Biological Monitoring Plans are being followed accurately
- Upcoming scope: road grading and preparation





# Snowdrop Road Project Update




Christmas Canyon Work



# Snowdrop Road Project Update

## UPCOMING SCOPE

- Complete drainage structures and cut off walls concrete work to 100%
- Road grading and preparation
- Arizona Concrete Crossing at Christmas Canyon

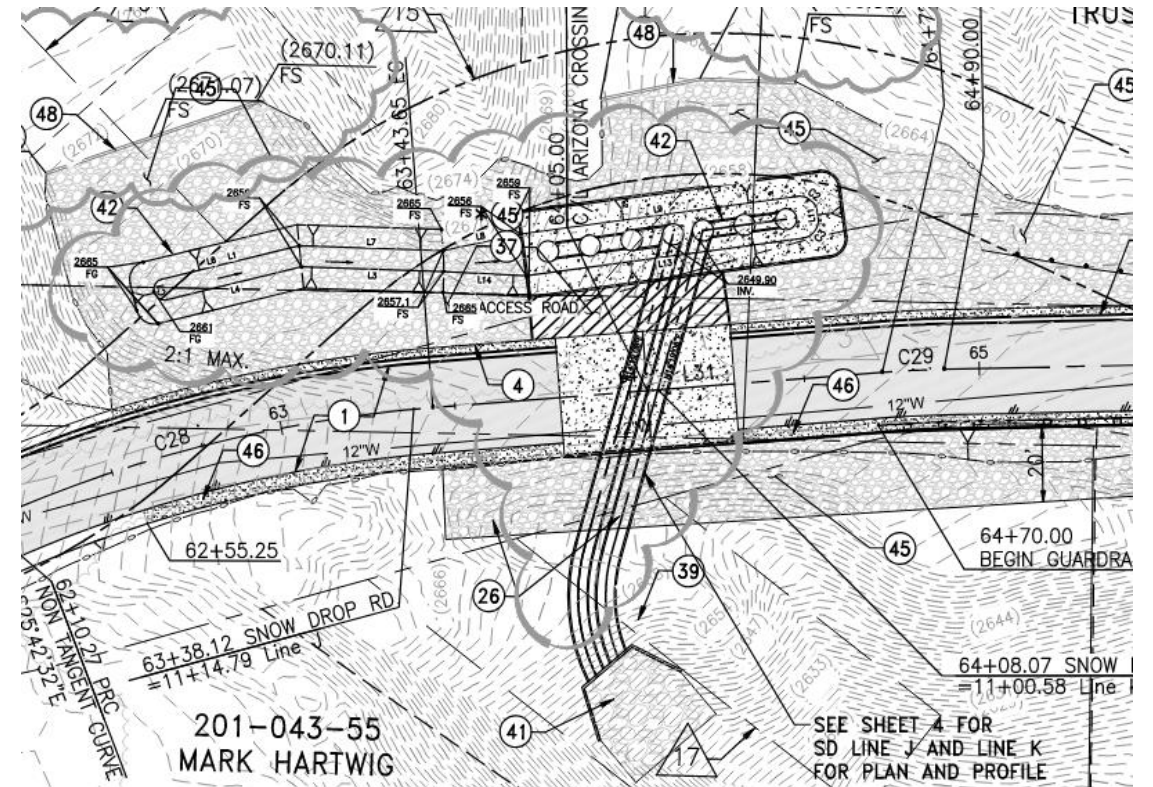



# Snowdrop Road Project Update

## Storm Water Management

- Storm Water Management plan is continuously monitored to ensure compliance to State Water Board requirements





## **Environmental Agreement** **and Biological Monitoring**

- Biological monitoring program did not identify any activity of nesting birds during the last reporting period from Dec 2021 to April 2022





## Easement Status

- Public Easements Status
  - Negotiations ongoing with LADWP to prepare 5-years access agreement to allow project construction while easement acquisition process continue
  - SCE parcel friendly condemnation process has been completed
- Private Easement Status
  - 1 Private easement remaining, negotiation in process

